


## Major Task Dependencies




## Fast Tracking Major Tasks


Project Start

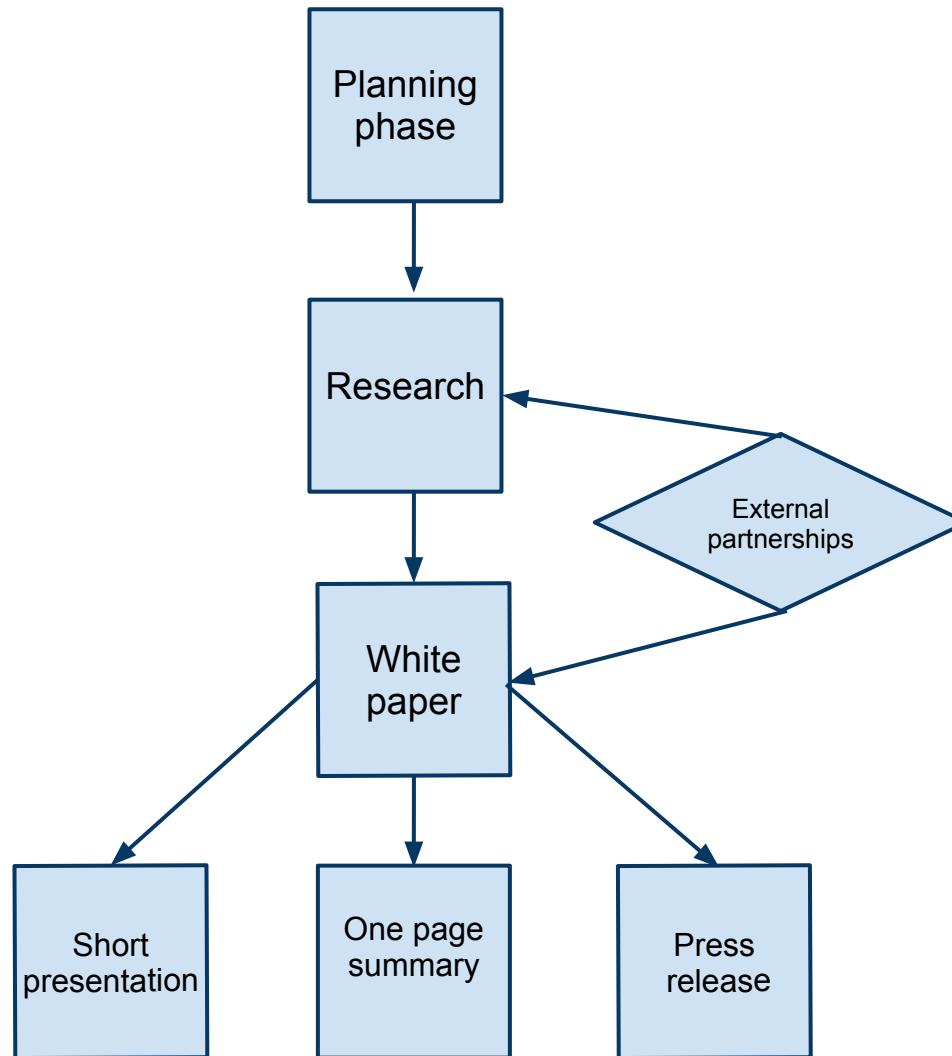


Research




White  
paper



Short  
presentation



One page  
summary



Press  
release

Project Finish






The major tasks start at approximately the same time and run in parallel. The mechanics of the written works can be laid down; content is added as it is passed along by the researchers.

Top Level Tasks as of Tue 4/19/11  
 Joint Written Project: Assessing Outbound Traffic to Uncover Advanced Persistent Threat (APT)

ID	Task Name	Duration	Start	Finish	% Comp.	Cost	Work
<b>0</b>	<b>Joint Written Project: Assessing O</b>	<b>40.75 days</b>	<b>Fri 4/15/11</b>	<b>Wed 5/25/11</b>	<b>0%</b>	<b>\$0.00</b>	<b>2,486 hrs</b>
<b>1</b>	<b>Kickoff project</b>	<b>3.63 days</b>	<b>Fri 4/15/11</b>	<b>Mon 4/18/11</b>	<b>0%</b>	<b>\$0.00</b>	<b>145 hrs</b>
<b>14</b>	<b>Create project plan</b>	<b>1.25 days</b>	<b>Mon 4/18/11</b>	<b>Tue 4/19/11</b>	<b>0%</b>	<b>\$0.00</b>	<b>0 hrs</b>
19	Submit project plan to Northcutt	0 days	Wed 4/20/11	Wed 4/20/11	0%	\$0.00	0 hrs
20	Project plan accepted	0 days	Wed 4/20/11	Wed 4/20/11	0%	\$0.00	0 hrs
<b>21</b>	<b>Establish external partnerships</b>	<b>2.25 days</b>	<b>Mon 4/18/11</b>	<b>Wed 4/20/11</b>	<b>0%</b>	<b>\$0.00</b>	<b>144 hrs</b>
<b>29</b>	<b>Research Technical Approaches fo</b>	<b>20 days</b>	<b>Wed 4/20/11</b>	<b>Tue 5/10/11</b>	<b>0%</b>	<b>\$0.00</b>	<b>480 hrs</b>
<b>35</b>	<b>Write white paper (Target: 10-30 pa</b>	<b>22.75 days</b>	<b>Wed 4/20/11</b>	<b>Fri 5/13/11</b>	<b>0%</b>	<b>\$0.00</b>	<b>1,274 hrs</b>
<b>48</b>	<b>Write one page summary</b>	<b>4.13 days</b>	<b>Fri 5/13/11</b>	<b>Tue 5/17/11</b>	<b>0%</b>	<b>\$0.00</b>	<b>99 hrs</b>
<b>55</b>	<b>Compile short presentation</b>	<b>5.63 days</b>	<b>Fri 5/13/11</b>	<b>Thu 5/19/11</b>	<b>0%</b>	<b>\$0.00</b>	<b>180 hrs</b>
<b>63</b>	<b>Write press release</b>	<b>5.13 days</b>	<b>Fri 5/13/11</b>	<b>Wed 5/18/11</b>	<b>0%</b>	<b>\$0.00</b>	<b>164 hrs</b>
70	Submit one page summary (for IDFAC	0 days	Wed 5/18/11	Wed 5/18/11	0%	\$0.00	0 hrs
71	Submit short presentation (10 PowerF	0 days	Wed 5/18/11	Wed 5/18/11	0%	\$0.00	0 hrs
72	Submit press release to Dean Svoboc	0 days	Wed 5/18/11	Wed 5/18/11	0%	\$0.00	0 hrs
73	Submit white paper to Northcutt and ii	0 days	Wed 5/18/11	Wed 5/18/11	0%	\$0.00	0 hrs
74	Write reflections essays	7 days	Wed 5/18/11	Wed 5/25/11	0%	\$0.00	0 hrs
75	Submit reflections essays to info@sar	0 days	Wed 5/25/11	Wed 5/25/11	0%	\$0.00	0 hrs
76	Joint Written Project is accepted and	0 days	Wed 5/25/11	Wed 5/25/11	0%	\$0.00	0 hrs

Milestones as of Tue 4/19/11  
Joint Written Project: Assessing Outbound Traffic to Uncover Advanced Persistent Threat (APT)

ID		Task Name	Duration	Start
2		Receive assignment via email	1 hr	Fri 4/15/11
20		Project plan accepted	0 days	Wed 4/20/11
19		Submit project plan to Northcutt	0 days	Wed 4/20/11
70		Submit one page summary (for IDFAQ)	0 days	Wed 5/18/11
71		Submit short presentation (10 PowerPoint content slides with Notes)	0 days	Wed 5/18/11
72		Submit press release to Dean Svoboda and info@sans.org	0 days	Wed 5/18/11
73		Submit white paper to Northcutt and info@sans.org	0 days	Wed 5/18/11
75		Submit reflections essays to info@sans.org	0 days	Wed 5/25/11
76		Joint Written Project is accepted and published	0 days	Wed 5/25/11

Milestones as of Tue 4/19/11  
Joint Written Project: Assessing Outbound Traffic to Uncover Advanced Persistent Threat (APT)

<b>Finish</b>	<b>Predecessors</b>	<b>Resource Names</b>
Fri 4/15/11		
Wed 4/20/11		
Wed 4/20/11	18	
Wed 5/18/11	63	
Wed 5/18/11	70SS	
Wed 5/18/11	71SS	
Wed 5/18/11	72SS	
Wed 5/25/11	74	
Wed 5/25/11	75	
